

MINUTEMAN VOCATIONAL TECHNICAL REGIONAL HIGH SCHOOL PROGRESS

March 19th, 2018 – April 23rd, 2018

SKANSKA

Gilbane

KÆSTLE BOOS
associates, inc
architects

 **MINUTEMAN**
A REVOLUTION IN LEARNING

April 3rd

View of Area A & B – East Elevation
Exterior light metal framing in
progress with beam infills and roof
parapet framing.



April 18th

View of Area A & B – North Elevation
Exterior light metal framing in
progress with beam infills and roof
parapet framing.



April 23rd

View of Area A & B – West Elevation

Exterior light metal framing in progress with beam infills and roof parapet framing.



April 23rd

View of Area A & B – High Roof

Exterior light metal framing in progress with roof parapet framing.



April 23rd

View of Area A & B – 2nd Floor
Metal deck prepped and
reinforced for slab on deck
placement.
Placement scheduled for 4/25



April 23rd
View of Area A & B – East
Elevation
Exterior CMU masonry back-up
walls in progress.



April 23rd
View of Area A & B – 1st Floor
Excavation/Backfill for installation of
underground utilities in progress.
Slab on grade placement scheduled
5/18



April 13th

View of Area G – Facing West
First concrete slab placement. Lower
level roof (Green Roof Area)

Upper slab on deck placement
scheduled 4/24



April 23rd

View of Area G – Lower Roof
Exterior light metal framing in
progress with roof parapet framing.



April 23rd
View of Area G – 1st Floor
Excavation/Backfill for installation of
underground utilities in progress.
Slab on grade placement scheduled
5/18



April 18th

View of Area F – East Elevation
Roof Parapet lay-out and prep for
framing in progress.



April 23rd

View of Area F – East Elevation
Roof Parapet framing & sheathing in
progress.



April 23rd

View of Area F – Roof Level


Roof Parapet framing & sheathing in progress.



April 3rd

View of Area C – Facing East

Final pieces of Roof steel being
set and bolted into place.

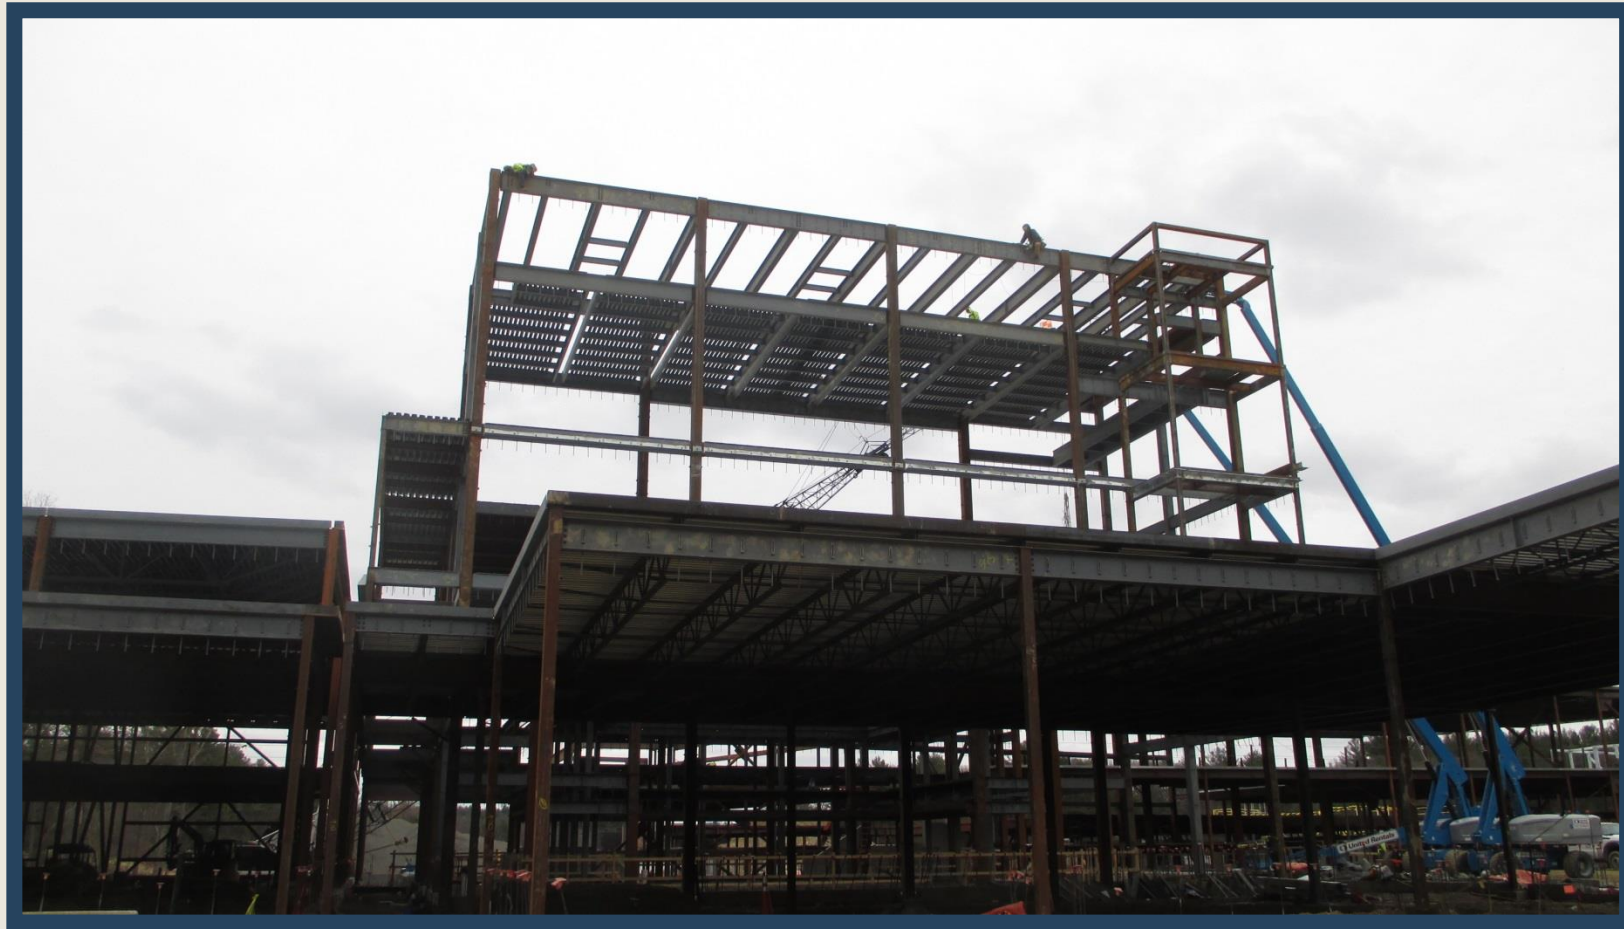

April 18th

View of Area C – Facing East

Decking & Detailing activities in
progress in Area C

Steel Erection continuing in Area D



April 12th
View of Area E – Facing West
Topping Off Ceremony



April 12th

View of Area E – Facing West

Topping Off Ceremony



April 12th
View of Area E – Facing West
Topping Off Ceremony



April/May Construction Schedule Look Ahead:

- **Area A+B**
 - Place concrete slab on deck on Level 2, scheduled for 4/25.
 - Complete excavation & backfill for under slab utilities.
 - Place concrete slab on grade, scheduled for 5/18.
 - Continue roof parapet framing and wood blocking.
 - Lay-out and install blocking for roof top mechanical equipment.
 - Continue exterior CMU masonry walls.
 - Commence roofing installation activities.
- **Area G**
 - Place concrete slab on deck on Level 2-Upper Level, scheduled for 4/24.
 - Complete excavation & backfill for under slab utilities.
 - Place concrete slab on grade, scheduled for 5/18.
 - Continue roof parapet framing and commence exterior framing on the 2nd Floor.
 - Lay-out and install blocking for roof top mechanical equipment.
 - Commence exterior CMU masonry walls.
- **Area E – Lower**
 - Place concrete slab on deck on Level 2-Bridge Level, scheduled for 5/1.
- **Area F**
 - Continue roof parapet framing. Lay-out and install blocking for roof top mechanical equipment.
- **Area C+D+E**
 - Area D complete steel erection on 4/27
 - Continue and complete steel detailing in remaining areas.
